

# Livingston Board of Education

## Annex Buildings – Construction Update

### Burnet Hill Elementary School and Hillside Elementary School

- Permit Drawings were submitted to the Township Building Department
  - **July 13, 2023** – Building, Plumbing, and Decks and Ramps
    - Contractor requested a partial review and release
  - **July 26, 2023** – Site and Electrical
- Both Buildings are fabricated and waiting to be delivered to sites.
  - Shipping from Georgia

### Hillside Elementary School

- Permits are to be released from Building Department this week
- Construction to start – **August 14, 2023** – underground work
- Week of **August 21, 2023** – Buildings delivered and set on site
  - Plumbing and electrical connections to follow
- **September 5, 2023 – First Day of School**
- Week of **September 5, 2023** – Installation of Decks, Ramps, and Steps
- Week of **September 11, 2023** – Final Inspections from Township
  - District will be able to move in right after



## Annex Buildings – Construction Update



# Livingston Board of Education


## Annex Buildings – Construction Update

### Burnet Hill Elementary School

- Awaiting release of permits from Township
  - Contractor anticipating permits week of **August 14, 2023**
- Construction will follow similar timeframes for installation
  - Construction would start – approx. **August 21, 2023** – underground scope of work
    - Site construction duration will be longer due to sewer ejector pit and pump
  - Approx. week of **August 28, 2023** – Buildings delivered and set on site
    - Plumbing and electrical connections to follow
  - **September 5, 2023 – First Day of School**
  - Approx. week of **September 11, 2023** – Installation of Decks, Ramps, and Steps
  - Approx. week of **September 18, 2023** – Final Inspections from Township
  - District will be able to move in right after

# Livingston Board of Education

## Annex Buildings – Construction Update

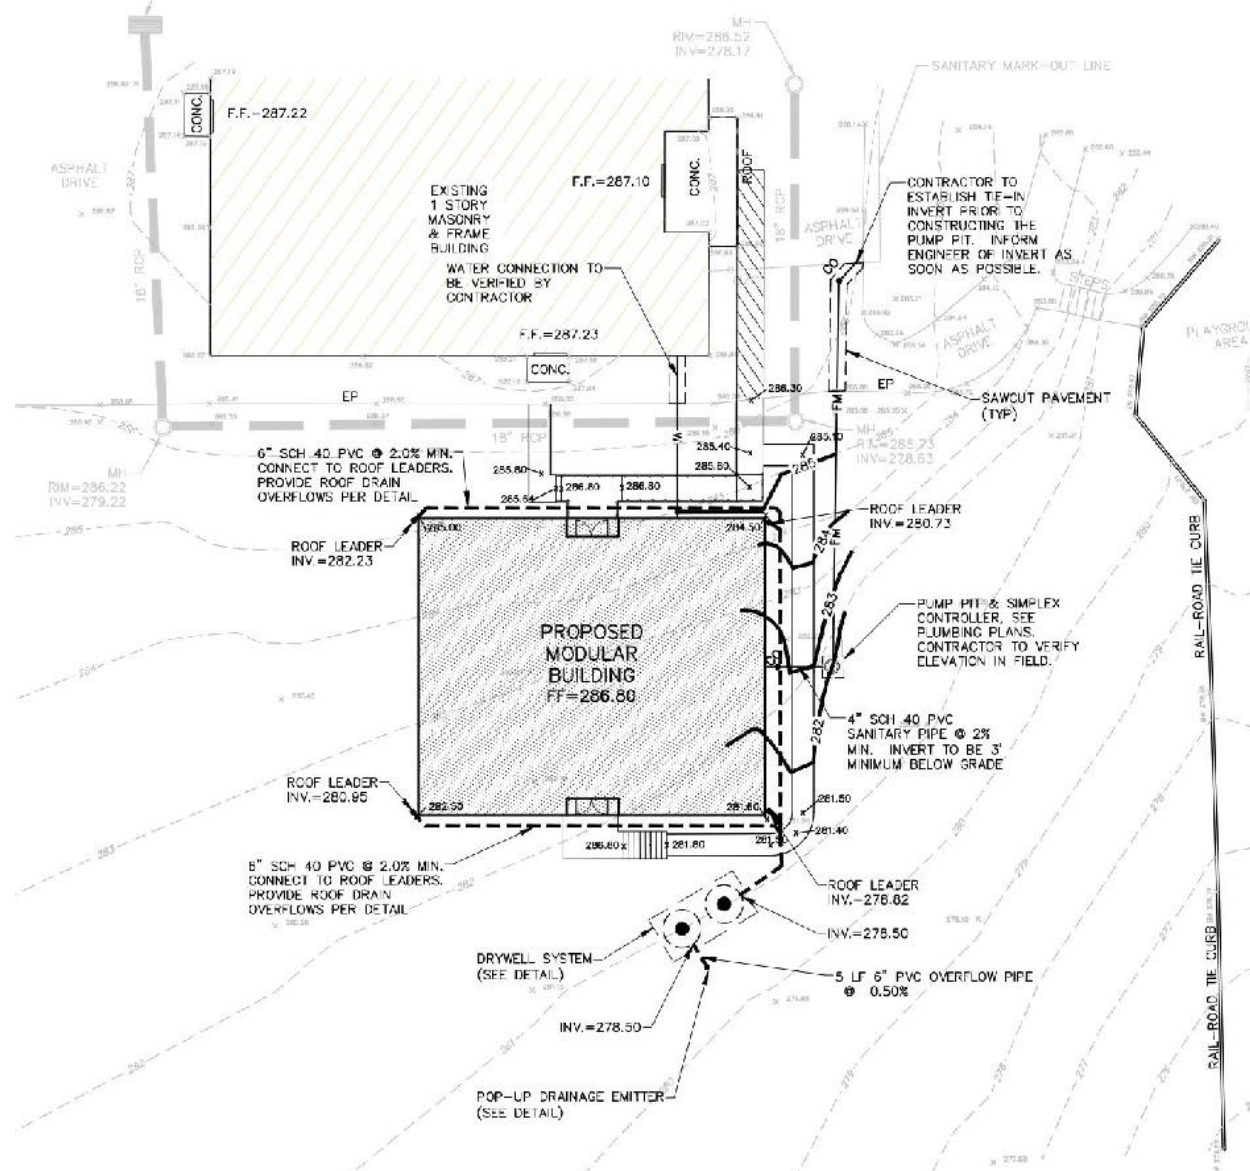

**Burnet Hill Elementary School – Site Plan**
